Final E-Bill
Recorded on:-

Job Number:- 002-24-000004
modified Cost Rs. 26.11 Lakhs

M. A. R. 57 (Rule 116) No. E
Measurement Book

Work order No:- BBMP/EE/YNK.D/EPMT-10/W.O/16/2023-24, Date 06/03/2024

Serial No. .....

Name of work Construction of R.O plant and other development works at JPN Colony census block no 89/1, 89/2 in Chowdeshwari ward No-02 of Yelahanka Subdivision

Name of Contractor or nature of Agency SRI. AKSHAY KUMAR H.B (AKSHAY CONSTRUCTIONS) No-209, Honnenahalli village, Doddaballapura main Road, Yelahanka Bangalore - 560064

Date of commencement of work.....

130201

Date	Full description, etc, of work	Dimensions Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	(1) Earth work excavation by manual means for drains, canals, waste weir, draft, approach channels, key trenches foundation of bridges and such similar works in all kinds of soils, as per drawing and technical Specifications. Quantity vide E-Bill:- 123.55 m^3 @ Rs. 225.45						27,854.23
	(2) Providing and laying in position plain cement Concrete for levelling Course for all works in foundation. The granite/trap/basalt Crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150mm Thickness etc as per Specifications.						

M. A. R. 57 (Rule 116) No. E

Measurement Book

Serial No. .....

130203

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(9) Providing and laying in position Reinforced cement Concrete for all Super Structures of building. Road works, water works, irrigation works & Super Structure works of bridges up to 3.50 mm height. etc as per Specifications. Quantity vide E-Bill :- 0.55 m³ @Rs. 8825.67						4854.12
	(10) Providing and laying in position Reinforced cement Concrete for all Super Structures of building. Road works, water works, irrigation works & Super Structure works of bridges up to 3.50 mm height. etc as per Specifications.						

M. A. R. 57 (Rule 116) **No. E**

Measurement Book

Serial No. .....

Name of work ..... From ..... To 130214

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(47) wiring for lighting/power circuit using one of FLRS PVC insulated 1100V grade, multis and copper with low Conductor Single Core Cable in open or Concealed Systems of wiring I Group A materials. b) 2.5 Sqmm.						
	Quantity vide E-Bill :-					135.00 mtrs	5840.10
	CRS. 43.26						
	(48) wiring for lighting/power circuit using one of FLRS PVC insulated 1100V grade, multis and copper with low Conductor Single Core Cable in open or Concealed Systems of wiring I Group A materials. c) 4 Sqmm.						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		Add	18% of GST charges RS:-				395304.28
(67)	BESCOM charges:-						18,000.00
			Grand Total RS:-				26,09,439.18

CERTIFICATE:-

1) Certified that the above work done is Satisfactory Complet

2) Certified that the, There is no debris have been cleared to

12/06/2024

Rama Sanjeeva
Asst. Executive Engi
Yelahanka Sub Divn
(BBMP) Ynk. Zn
12/06/2024

M. A. R. 57 (Rule 116) **No. E**

Measurement Book

Serial No. .....

130220

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

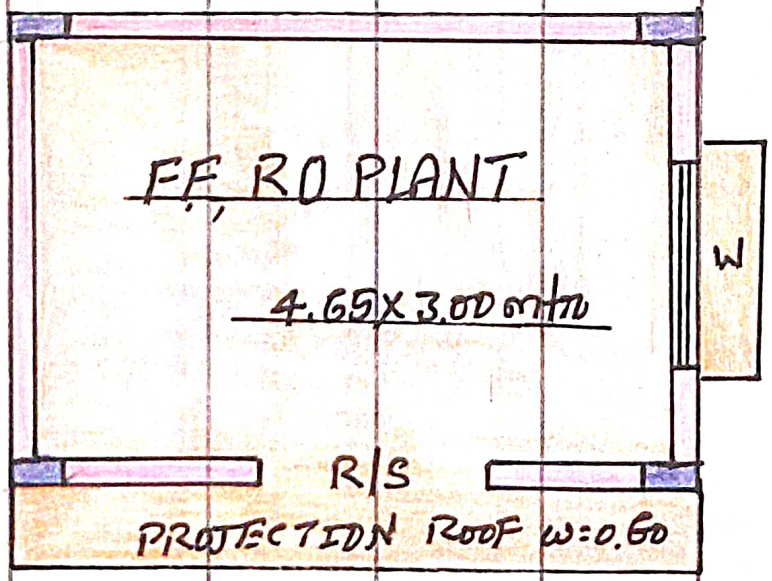

SKETCH :-

INDEX :-

R/S :- 1X1.90X2.15

W :- 1X0.90X1.20

Columns :- 4X0.45X0.20

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Ynk. Zn)
Yelahanka, Bangalore
